


Weekly Project Report | Report #23 | Date: July 10, 2017



Half Day – Exterior, 2nd Floor Addition

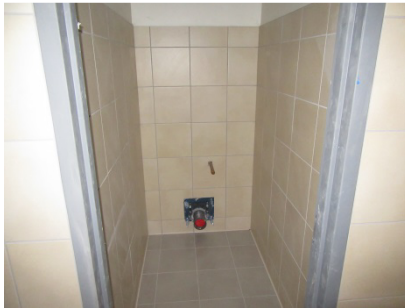

Half Day – Addition Restroom Stall, Tile



Sprague – Existing School Renovation



Sprague – Addition, Exterior

Safety Notices for Students and Staff:

- Please be aware of construction-related vehicles entering and exiting the entrance to the Half Day Intermediate School site on the north driveway off of Olde Half Day Road.
- Please be aware of construction-related vehicles entering and exiting the entrance to the Laura B. Sprague School site off of Kings Cross Drive.
- Please do not enter the areas within the fencing. Please do not congregate near the construction site entrances.
- Site access is restricted to contractors and authorized personnel. **Non-Construction Vehicles are not allowed on or through the site.**

Project Safety:

The construction team has worked a total of 130 of 134 Days incident and injury free and without a lost time accident on the project through July 09, 2017.

Week In Review - Week of July 03, 2017

- Half Day Main Addition: Continued with ceilings on level 2, MEP trim on level 1, and ceramic tile on level 1. Continued with roof edge coping and exterior painting.
- Half Day Existing Renovation: Continued with MEP rough-in and framing on both levels. Installed attic steel and MEP equipment.
- Half Day Office Addition: Masonry walls were installed; made ready for roof steel.
- Sprague Main Addition: Level 1 painting began. Level 2 wall finishing continued.
- Sprague Existing Renovation: Drywall began. MEP rough-in continued.

Week Major Activity Look-ahead - Week of July 10, 2017

Half Day School:

- Addition: Continue with MEP trim, painting, ceilings, and ceramic tile on Levels 1 and 2.
- Addition: Continue with exterior painting and final exterior windows.
- 2nd Floor Office Addition: Install roof steel and begin roofing and facebrick.
- Existing School Renovation: Continue with MEP rough-in, framing, and begin drywall.

Laura Sprague School:

- Addition: Continue with painting. Begin ceilings and ceramic tile on Level 1.
- Addition: Prepare for elevator installation. Begin stairs.
- Addition: Roof edge coping. Window caulking.
- Existing School Renovation: Continue with drywall and prepare for painting and ceilings.
